
Sprint 2 Schedule Report

Network Diagram and Critical Path:

For our sprint, some tasks had to be finished before others could start. For example, we had to finish the backend for both the driver and passenger side of the app, before we could implement the Ride History GUI and create a list for the completed for both driver and passenger.

Task Dependencies: For this Sprint we had 18 tasks. Some tasks depended on others. For example, we could not build the User Interfaces (UIs) until the Data Models (like Person.java or Ride.java) were finished. We also could not start integration testing until the features were fully coded.

DIAGRAM IS BELOW

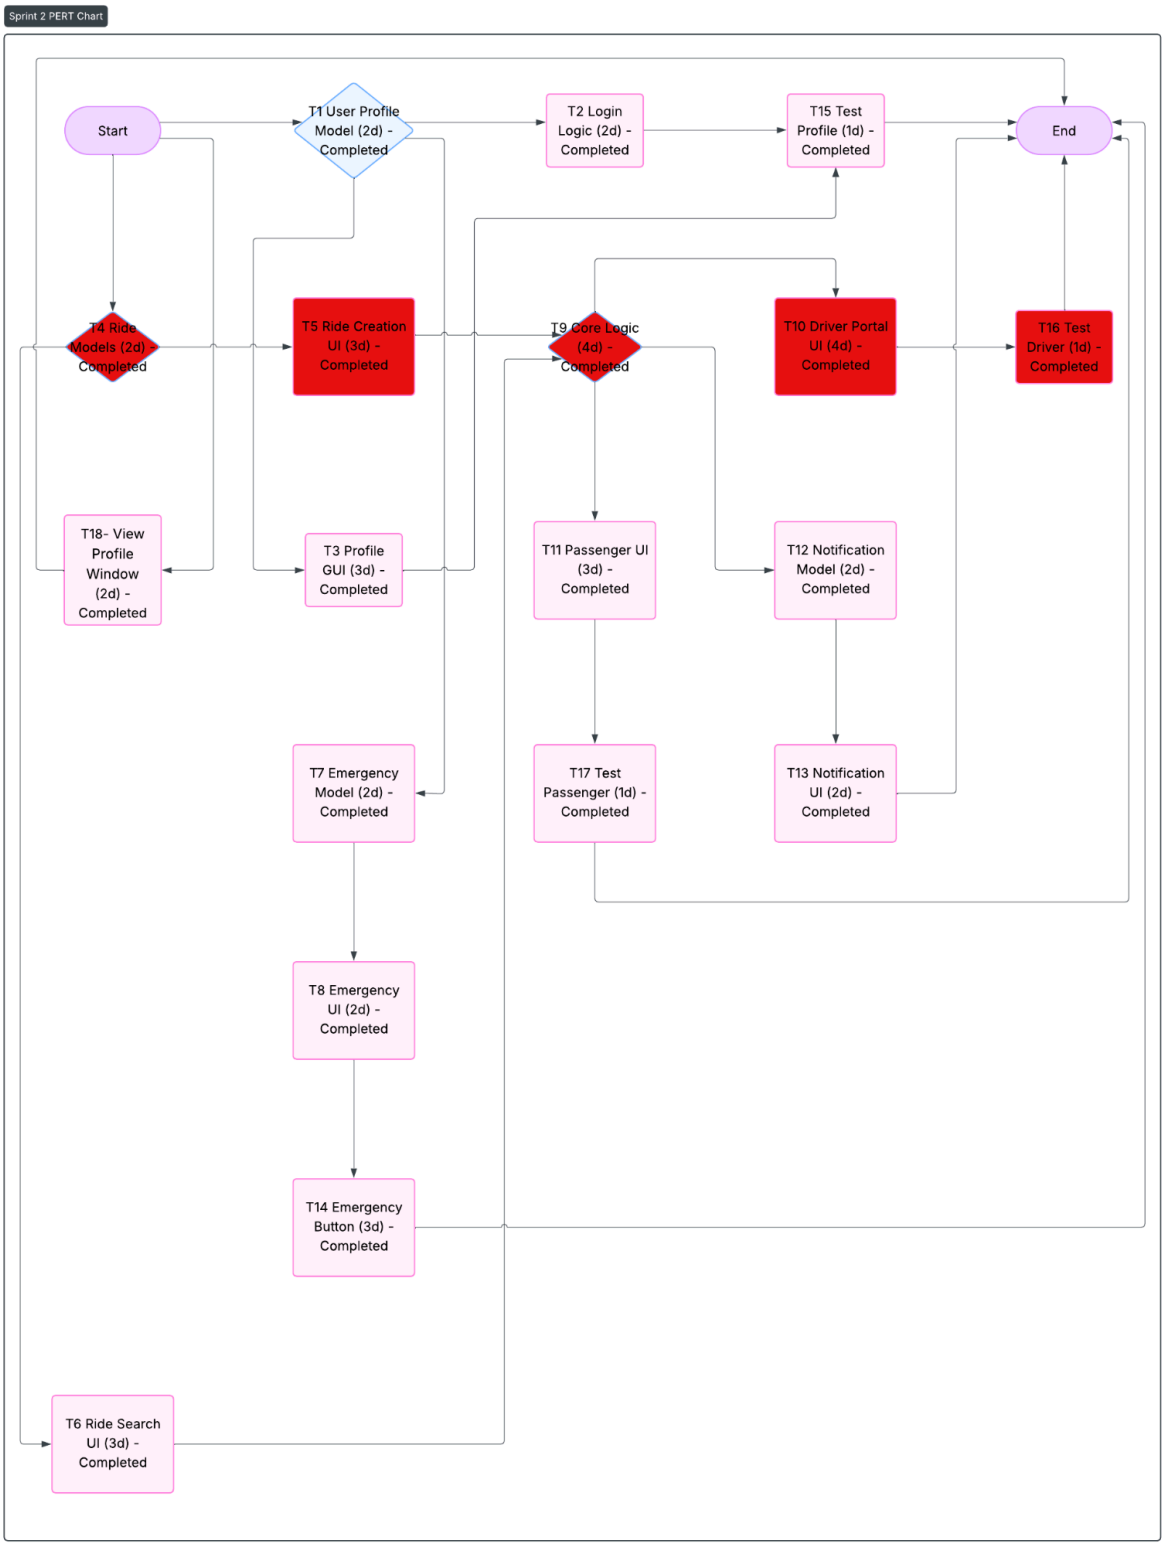

The Critical Path was the longest sequence of connected tasks, which took 14 days. This means if any task on this path was late, the whole sprint would be late.

Our Critical Path:
T4 (Ride Models) (Creating the backend database structure for Rides and Requests) , T5 (Ride Creation UI) (Building the screen where drivers input ride details), T9 (Core Logic) (Writing the server code that calculates seats and links passengers to drivers) , T10 (Driver Portal) (Building the dashboard where drivers accept requests), T16 (Driver Test) (Testing the full workflow to ensure data is saved correctly).

How We Stayed on Schedule

We had a tight 14-day timeline with no extra time, but we still finished all 18 tasks by:

Working at the same time: 2 people worked on the main Driver UI and Core Logic tasks (T9/T10) while others worked on smaller tasks like the Emergency Button (T14) and emergency UI (T8). This helped us move faster.

We Tested early: We tested features such as “Login” (T15) right after building them. This lets us catch problems early, like the NULL driver_id bug, and fix them quickly in our backend by making sure classes are using the same parameters.

What Went Wrong (Risks) & Lessons Learned

What Went Wrong: Halfway through the sprint, we added a new task (T18 – View Profile Window). Based on the code we just added, this included the new “My Profile” tab and the ViewProfileGUI window. This wasn’t part of our original plan, which only included a simple “Profile Customization” screen. Adding new work in the middle of a sprint is risky because it can take time away from more important tasks.

How We Handled It: We were able to finish T18 because it was a small, standalone UI task. We assigned it to a team member who had already completed their “User Profile” work, so it did not slow down the main Driver Flow.

What We Learned: We learned that adding new features during a tight schedule can cause delays.
