
Sprint 3 Schedule Report

Network Diagram and Critical Path:

For this sprint, some tasks had to be finished before we could start others. For example, we needed to finish the Ratings feature first, then build the In-App Chat, and only after that could we work on the Payment system. The Weather feature was the last step in this chain, so it depended on all the tasks before it.

We also had another set of tasks starting from Google Maps (US 13), which led to Carbon Footprint (US 12) and Lost & Found (US 16). These tasks were separate from the main path of Ratings → Chat → Payment → Weather.

DIAGRAM IS BELOW

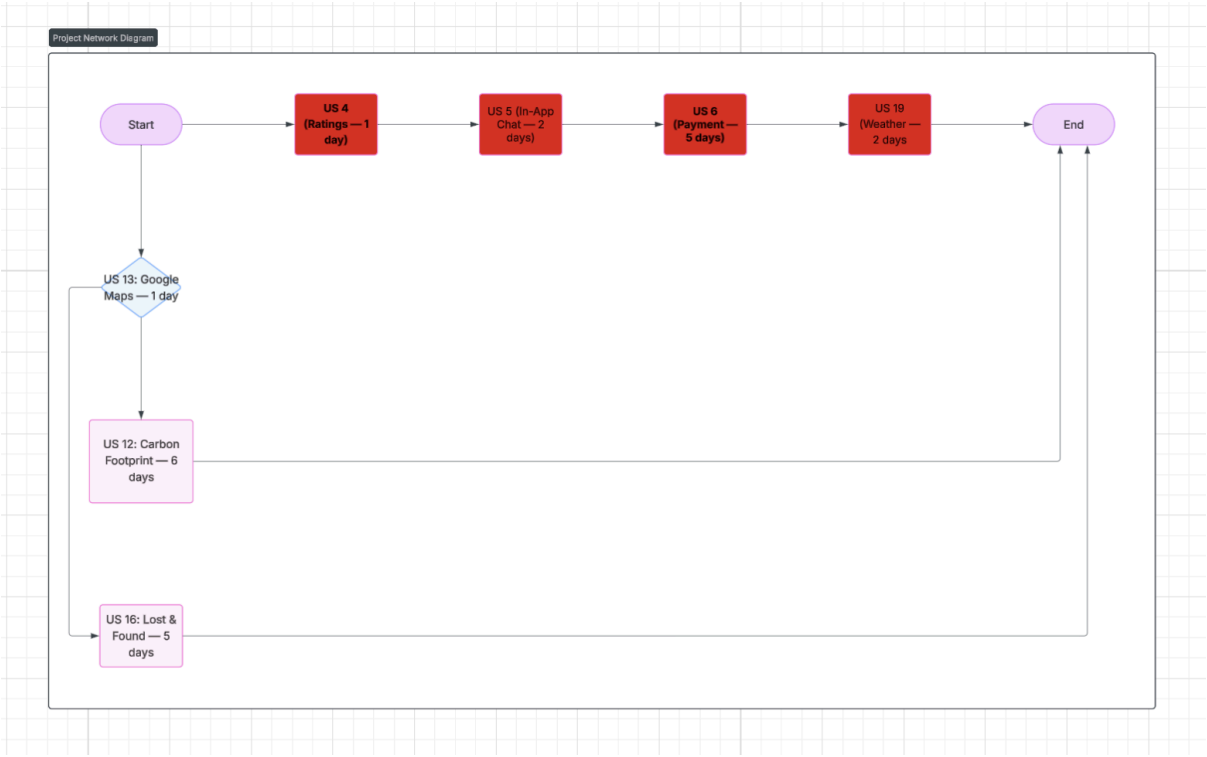

The Critical Path was the longest chain of tasks, and it took 10 days to finish. This meant that if any task on this path was delayed, the entire sprint would be delayed as well.

Our Critical Path:
Our Critical Path included the tasks for Ratings (US 4), In-App Chat (US 5), Payment (US 6), and Weather (US 19). These had to be completed in this exact order because each one depended on the one before it. Ratings had to be set up first, then the Chat feature, followed by the Payment system, and finally the Weather feature. Since all of these tasks were linked, a delay in any one of them would delay the entire sprint.

How We Stayed on Schedule

We had a tight 10-day timeline with no extra room, but we stayed on track by working in parallel. While one part of the team focused on the main critical path tasks Ratings, Chat, Payment, and Weather,other team members worked on smaller tasks like Google Maps, Lost & Found, and Carbon Footprint. We also tested our features as soon as we finished them. For example, after completing Ratings and Chat, we tested both right away to make sure they worked properly before moving on. This helped us catch issues early and avoid bigger problems later, especially when working on the Payment system, which depended on everything before it.

What Went Wrong & Lessons Learned:

What Went Wrong:
One problem we faced was that the Payment task took longer than we expected. Since Payment was in the middle of the critical path, any delay there would have delayed Chat, Weather, and the whole sprint. Another issue was that Google Maps (US 13) had to be done before Carbon Footprint and Lost & Found, so if US 13 was late, the other two tasks would have been late as well.

How We Handled It:
To deal with this, we started Payment early and gave it enough time. We also made sure Google Maps was done first so that the other tasks depending on it could start on time. By spreading the work across the team, everything kept moving.

What We Learned:

We learned that when a task is important to many other tasks, it needs extra attention. Keeping track of these key tasks helped us finish the sprint on time.
