
Team Name: CampusCommute
Sprint: Sprint 2
Sprint Duration: November 4th - November 17th

Burndown chart:

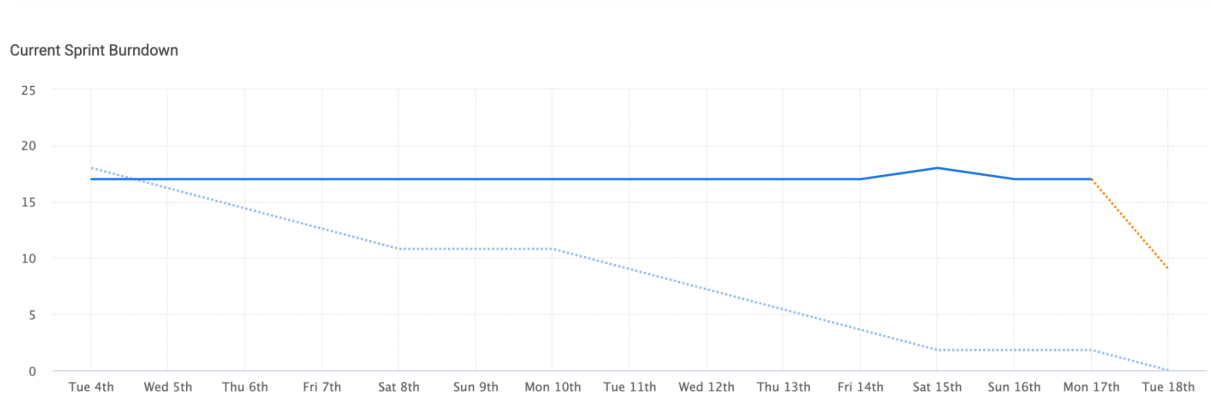

To open this in trello click the button on the left of “Power-ups” labelled “Corrello” click “Dashboard” and then on the left hand side click “Sprint Burndown”. You may have to click on the tab labelled “Previous sprints” to view this chart depending on when you access it.

1. Comments on the Sprint Burndown Chart

The provided brundown chart tracks the remaining effort in user stories against the time available in the sprint. The solid blue line represents the Total Scope and the Dotted Blue Line represents the actual remaining effort.

Initial Scope: The sprint began on November 4th with 17 user stories planned for completion. However, on November 15th, the total scope line increased, indicating that 1 user story was added during the sprint bringing the total committed scope to 18 user stories.

- The most notable feature is the significant gap between the expected burndown and the recorded burndown for most of the sprint.
- The plateau is not representative of actual work stagnation. It is a consequence of the team’s policy to delay moving stories to the “Completed” column in Trello until the very end of the sprint, when we are certain there are no further changes necessary.

Late Burndown: The actual reduction in remaining work occurs dramatically over the last few days. By the end of the sprint, the team has completed 9 user stories, leaving 9 user stories to be completed for the next sprint.

Conclusion: The chart visually shows a slow start and a late completion, but the team confirms that the burndown line is not an accurate representation of our consistent daily effort. Despite the chart not showing it, consistent work was performed and future sprints will enforce a more

real-time tracking policy. We will be sure to mark tasks as “Completed” or “Testing” more accurately to ensure the burndown chart provides a more accurate measure of progress.

2. Velocity Comparison and Explanation

The team's performance demonstrates a substantial increase in throughput, completing 9 user stories in Sprint 2 compared to only 3 in Sprint 1. This significant acceleration confirms that the team’s actual velocity has increased dramatically.

Explanation for Increased Velocity
The improved efficiency achieved in Sprint 2 are due to the following factors:

- Improved Team Coordination: Tasks were assigned more strategically and standups led to faster identification and resolution of blockers.
- Technical Familiarity: The team became more familiar with the architecture (including Spring Boot and MySQL integration). Along with this, the necessary refactoring and foundation fixes completed in Sprint 1 saved a lot of time in Sprint 2 as it led to implementing new features quickly and efficiently.
- Clearer Scope: the learning curve associated with the project’s foundational concepts was overcome in Sprint 1. Sprint 2 tasks focused more on feature implementation rather than architectural setup, leading to more tasks being completed.
