
Team Name: CampusCommute
Sprint: Sprint 3
Sprint Duration: November 18th - December 1st

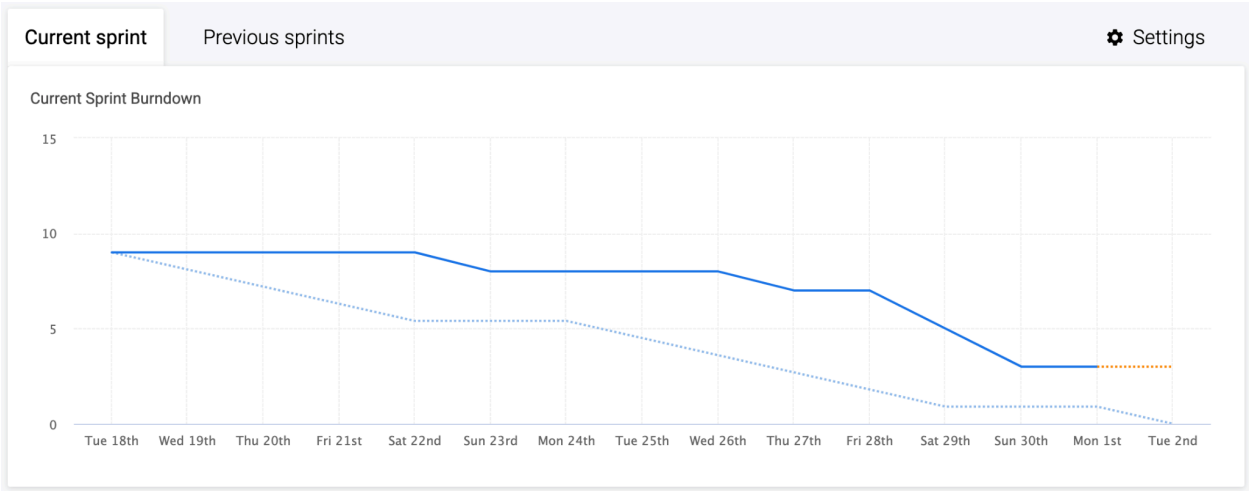

To open this in trello click the button on the left of “Power-ups” labelled “Corrello” click “Dashboard” and then on the left hand side click “Sprint Burndown”. You may have to click on the tab labelled “Previous sprints” to view this chart depending on when you access it.

1. Comments on the Sprint Burndown Chart

The provided burndown chart tracks remaining effort for Sprint 3. The solid blue line represents the Total Scope, and the dotted blue line represents the Actual Remaining Effort.

Initial Scope: The sprint began on November 18th with 9 user stories planned for completion. This scope aligns perfectly with the 9 stories carried over from the incomplete Sprint 2.

Scope Stability: The solid blue line remains stable at 9 user stories for the first few days of the sprint until November 22 when our first user story of the sprint gets completed and the line drops. After this, there was a long plateau until November 26 when our group started showing more steady progress. From here on out the group starts completing a lot more user stories and is more consistently working.

The Sprint 3 Burndown Chart demonstrates significantly better tracking and predictability compared to Sprint 2. The consistent, staggered burndown is a much more accurate reflection of continuous daily effort. The team showed excellent discipline in adjusting the scope mid-sprint to ensure a high probability of completion, demonstrating better Scrum habits within our group.

2. Velocity Comparison and Explanation

The team’s performance remained consistent in this sprint as we completed 6 user stories compared to the 9 completed in the last sprint. This can be attributed to the leftover user stories

being more difficult and the group overall becoming more busy as the semester comes to an end.

Explanation for Decreased Velocity

The slight decrease in completed user stories is not a sign of reduced efficiency, but rather a reflection of better planning and higher quality work driven by the following factors:

- Accurate Planning for Carry-Over: Sprint 3's initial scope was exactly the 9 user stories carried over from Sprint 2. The team recognized the complexity of this remaining work (such as Driver Ratings, Carbon footprint calculations, etc.). By only committing to the essential 6 user stories of the leftover 9, the team ensured the quality completion of the critical features.
- Increased Story Complexity: The final 9 stories from Sprint 2 were generally the most complex. Committing to 6 of these complex stories instead of all 9 stories resulted in a high-value output, even if the raw story count is slightly lower than the volume achieved during Sprint 2.
- Focus on Real-Time tracking: The team successfully enforced the proper use of real-time status updates when tracking on Trello. We moved tasks to "in progress" or "testing" or "completed" more accurately than we did in Sprint 2. This eliminated the misleading plateau observed in Sprint 2, which proves that the team's execution remained efficient and consistent throughout Sprint 3.
